



Fort Wayne Riverfront Phase 1

Park Foundation Pavilion



Riverfront
FORT WAYNE
Always moving.

Weekly Progress Update for Week Ending 6/24/18

Past Two Weeks of Progress

- | | |
|--|---|
| <ul style="list-style-type: none"> * Continue Metal Stud Framing for Canopy Soffit * Installation of F1 Fixtures at Pavilion Canopy * Final Clean Concrete Seat Walls * Install Ice and Water Shield above Limestone Cladding for Pre-Finished Flashing * Electrical Ceiling Rough-In | <ul style="list-style-type: none"> * Continue Metal Stud Framing Throughout Pavilion (Event Space Ceiling/Vestibule) * Finish Mudding and Sanding Interior Gypsum Board Walls * Continue Installing Sheathing and Furring at Canopy Soffit * Install Plywood Sheathing/Rigid Foam Board Insulation at Metal Wall System Detail * Start Installation of Pre-Finished Fascia |
|--|---|

Next Week Look Ahead

- | | |
|---|---|
| <ul style="list-style-type: none"> * Continue Metal Stud Framing for Canopy Soffit * Continue Electrical Ceiling Rough-In * Install Ice and Water Shield above Limestone Cladding for Pre-Finished Flashing * HVAC Duct/Plumbing Insulation | <ul style="list-style-type: none"> * Continue Metal Stud Framing Throughout Pavilion (Event Space Ceiling/Vestibule) * Final Clean Concrete Seat Walls * Install Plywood Sheathing/Rigid Foam Board Insulation at Metal Wall System Detail * Continue Installation of Pre-Finished Fascia |
|---|---|

Milestone Events

- | | |
|---|--|
| <ul style="list-style-type: none"> * Finish Final Clean of Pavilion Seat Walls Week of 6/25/18 | <ul style="list-style-type: none"> * Start Limestone Week of 7/2/18 |
|---|--|

Progress Photos





Fort Wayne Riverfront Phase 1


Park Foundation Pavilion



Riverfront
FORT WAYNE
Always moving.

Weekly Progress Update for Week Ending 6/24/18

Progress Photos Continued

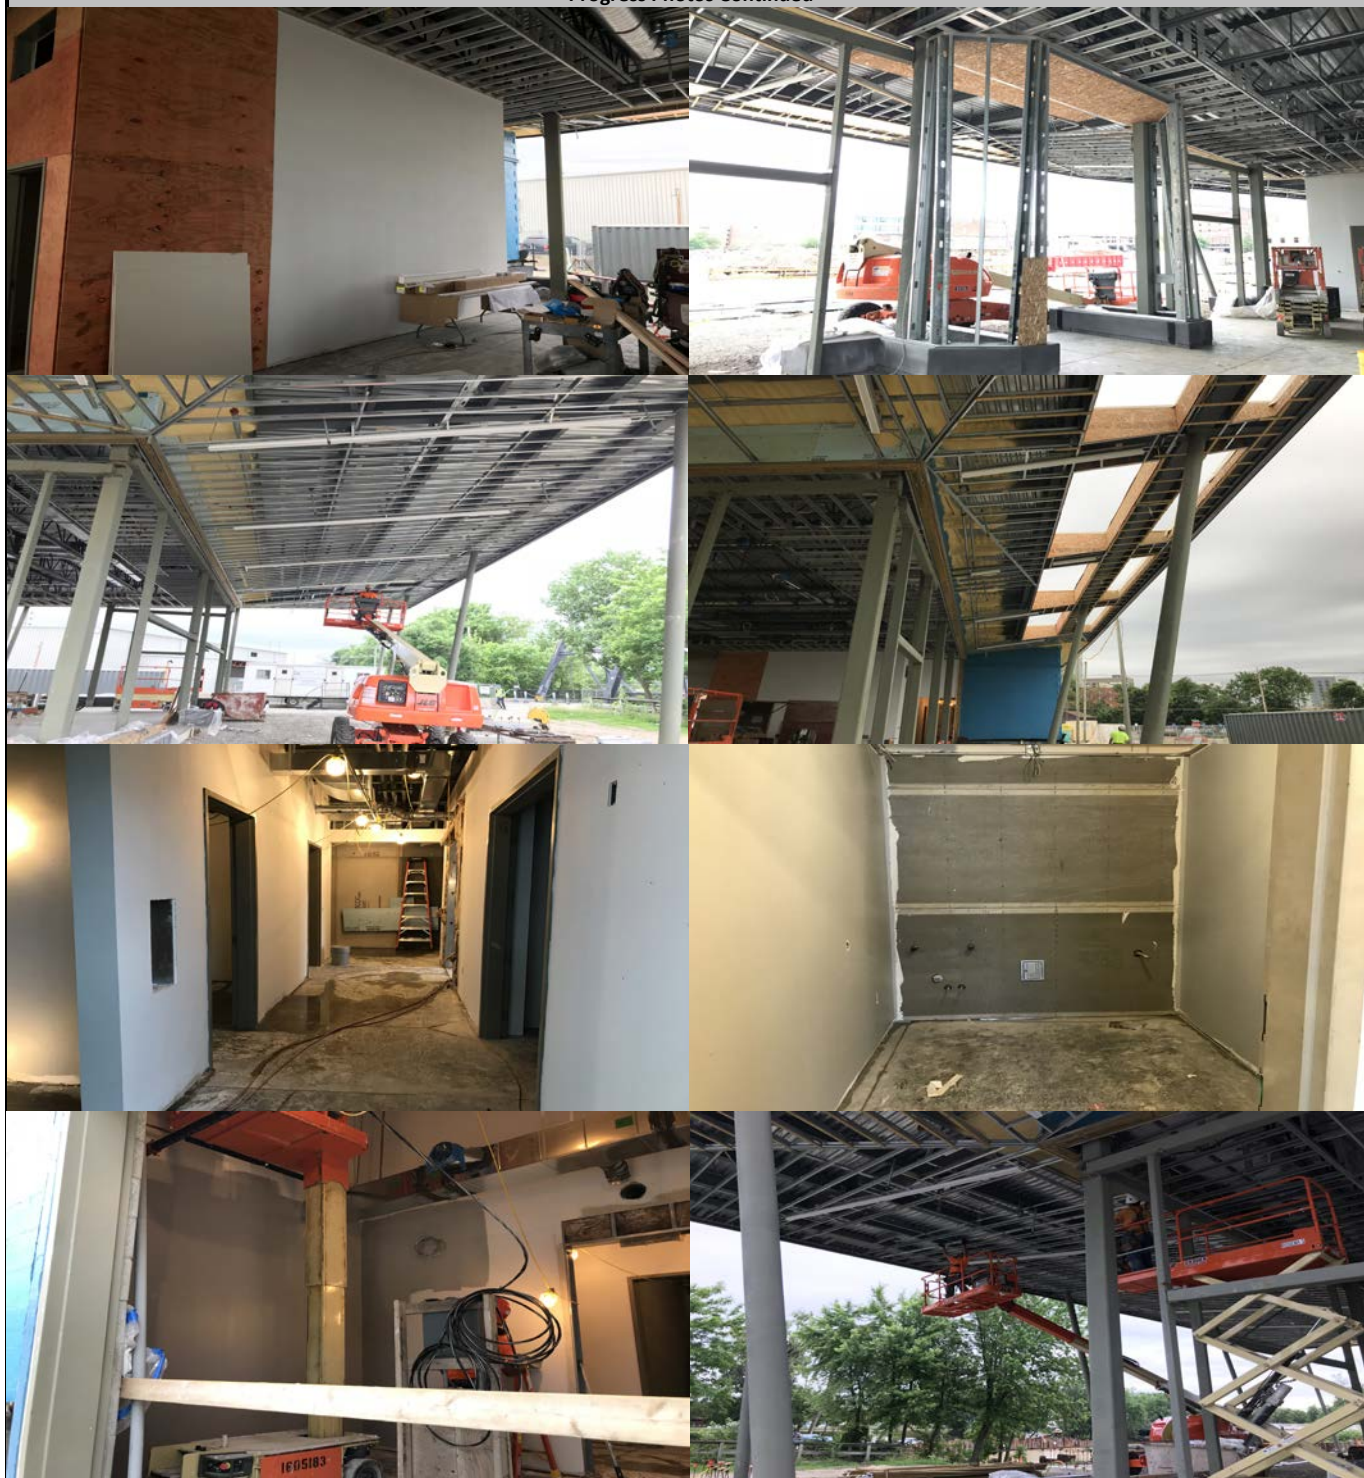



Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 6/24/18

Past Two Weeks of Progress

- | | |
|---|--|
| <ul style="list-style-type: none"> * Continue Driving H-Piles at South Shore Seawall (Vertical/Battered) * Pour Foundation at Abutment #2/ Pour Pier #22 & Pier #21 * Continue Excavation Within North Shore Seawall Cofferdam * Install Sheet Pile Bracing at North Seawall Cofferdam * Cut H-Piles to Specified Elevation at South Shore Seawall | <ul style="list-style-type: none"> * Continue Dewatering South Cofferdam/Pier #22/ Pier#15-#21/North Cofferdam * Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam * Haul off Excess Spoils Onsite and Store Required Spoils at North Shore Laydown Area * Start Driving H-Piles to Final Bearing at the North Shore Seawall |
|---|--|

Next Week Look Ahead

- | | |
|--|--|
| <ul style="list-style-type: none"> * Continue Driving H-Piles at South Shore Seawall (Vertical/Battered) * Continue Excavation Within North Shore Seawall Cofferdam * Continue Installation of Sheet Pile Bracing at North Seawall Cofferdam * Cut H-Piles to Specified Elevation at South Shore Seawall | <ul style="list-style-type: none"> * Continue Dewatering South Cofferdam/Pier #22/ Pier#15-#21/North Cofferdam * Excavation/Up-Keep on South Bank Within the South Seawall Cofferdam * Haul off Excess Spoils Onsite and Store Required Spoils at North Shore Laydown Area * Strip Forms at Abutment #2/ Pier #22 & Pier #21 |
|--|--|

Milestone Events

- * Poured Abutment #2 Foundation and Pier #22/Pier #21 the Week of 6/18/18

Progress Photos





Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 6/24/18

Progress Photos Continued

