

Project Number - 16-0864-Q

Page 1



FORT WAYNE
PARKS AND
RECREATION

Fort Wayne Riverfront Phase 1

Park Foundation Pavilion





Riverfront
FORT WAYNE
Always moving.

Weekly Progress Update for Week Ending 9/9/18

Past Week of Progress

- * Continue Installation of Limestone Cladding
- * Start Curtain Wall Framing in Event Space
- * Continue Mud/Sand/Paint All Unfinished Gypsum Board Within the Pavilion
- * Excavate and Install Water Line to Pavilion

- * Touch-Up Finish Coat at Interior Columns
- * Continue Miscellaneous Plumbing Rough-In
- * Continue Miscellaneous Electrical Rough-In/ Lighting Fixture Installation
- * Continue Install Rigid Extruded Insulation Board at Vestibule Entry

Next Week Look Ahead

- * Continue Installation of Limestone Cladding
- * Continue Curtain Wall Framing in Event Space
- * Continue Mud/Sand/Paint All Unfinished Gypsum Board Within the Pavilion
- * Excavate and Install Water Line to Pavilion
- * Continue Miscellaneous Plumbing Rough-In

- * Touch-Up Finish Coat at Interior Columns
- * Start on Canopy T&G Cedar Soffit
- * Continue Miscellaneous Electrical Rough-In/ Lighting Fixture Installation
- * Finish Installation Rigid Extruded Insulation Board at Vestibule Entry

Milestone Events

* Started Event Space Curtain Wall Week of 9/3/18

* Week of 9/10/18 Start Exterior Canopy Pre-Finished T&G Cedar Soffit

Park Foundation Pavilion Progress Photos





Fort Wayne Riverfront Phase 1

Park Foundation Pavilion



Weekly Progress Update for Week Ending 9/9/18

Park Foundation Pavilion (Continued)





Fort Wayne Riverfront Phase 1
Park Foundation Pavilion



Weekly Progress Update for Week Ending 9/9/18

Past Week of Progress

- | | |
|--|---|
| <ul style="list-style-type: none">* Continue Flatwork Prep at South Seawall* Form and Prep 1st Row of Lounger and Seatwalls on South Seawall* Continue to Form 1st Row of Lounger and Seatwalls on South Shore* Continue Form and Prep of Abutment #1 Wall Sections* Form and Prep Piers #15 and #16* Removal of North Side Sheets at North Seawall Cofferdam | <ul style="list-style-type: none">* Complete Backfill at North Seawall and Around Piers #5, #6, & #7* Excavate and Drive Piles for Piers #2, #11, #12, #13 and #14 and Temporarily Backfill* Complete Form, Prep, and Pour of Abutment #2 Wall Sections* Pour Bandshell Foundation* Demolition of Wells Street Asphalt* Excavate Footing for Free Standing Wall at West End of South Seawall |
|--|---|


Next Week Look Ahead

- | | |
|---|--|
| <ul style="list-style-type: none">* Continue Flatwork Prep at South Seawall* Complete Prep and Pour of Pier #15 and #16* Pour Cheek Wall Along 1st Row of Lounger and Seatwalls on South Seawall* Start Fine Grading for Flatwork at North Seawall* Prep and Pour Footing for Free Standing Wall at West End of South Seawall | <ul style="list-style-type: none">* Complete Form, Prep, and Pour of Abutment #1 Wall Sections* Form, Prep, and Pour Columns #15 and #16* Continue Form/Prep at 1st Row of Lounger and Seatwalls and Start Pouring Sections* Start to Form Along Face of North Seawall for Flatwork |
|---|--|

Milestone Events

- | | |
|--|--|
| * Completed Driven Piles on Overall Project Week of 9/3/18 | * Pour Columns #15 and #16 Week of 9/10/18 |
|--|--|

South Seawall/Site Progress Photos

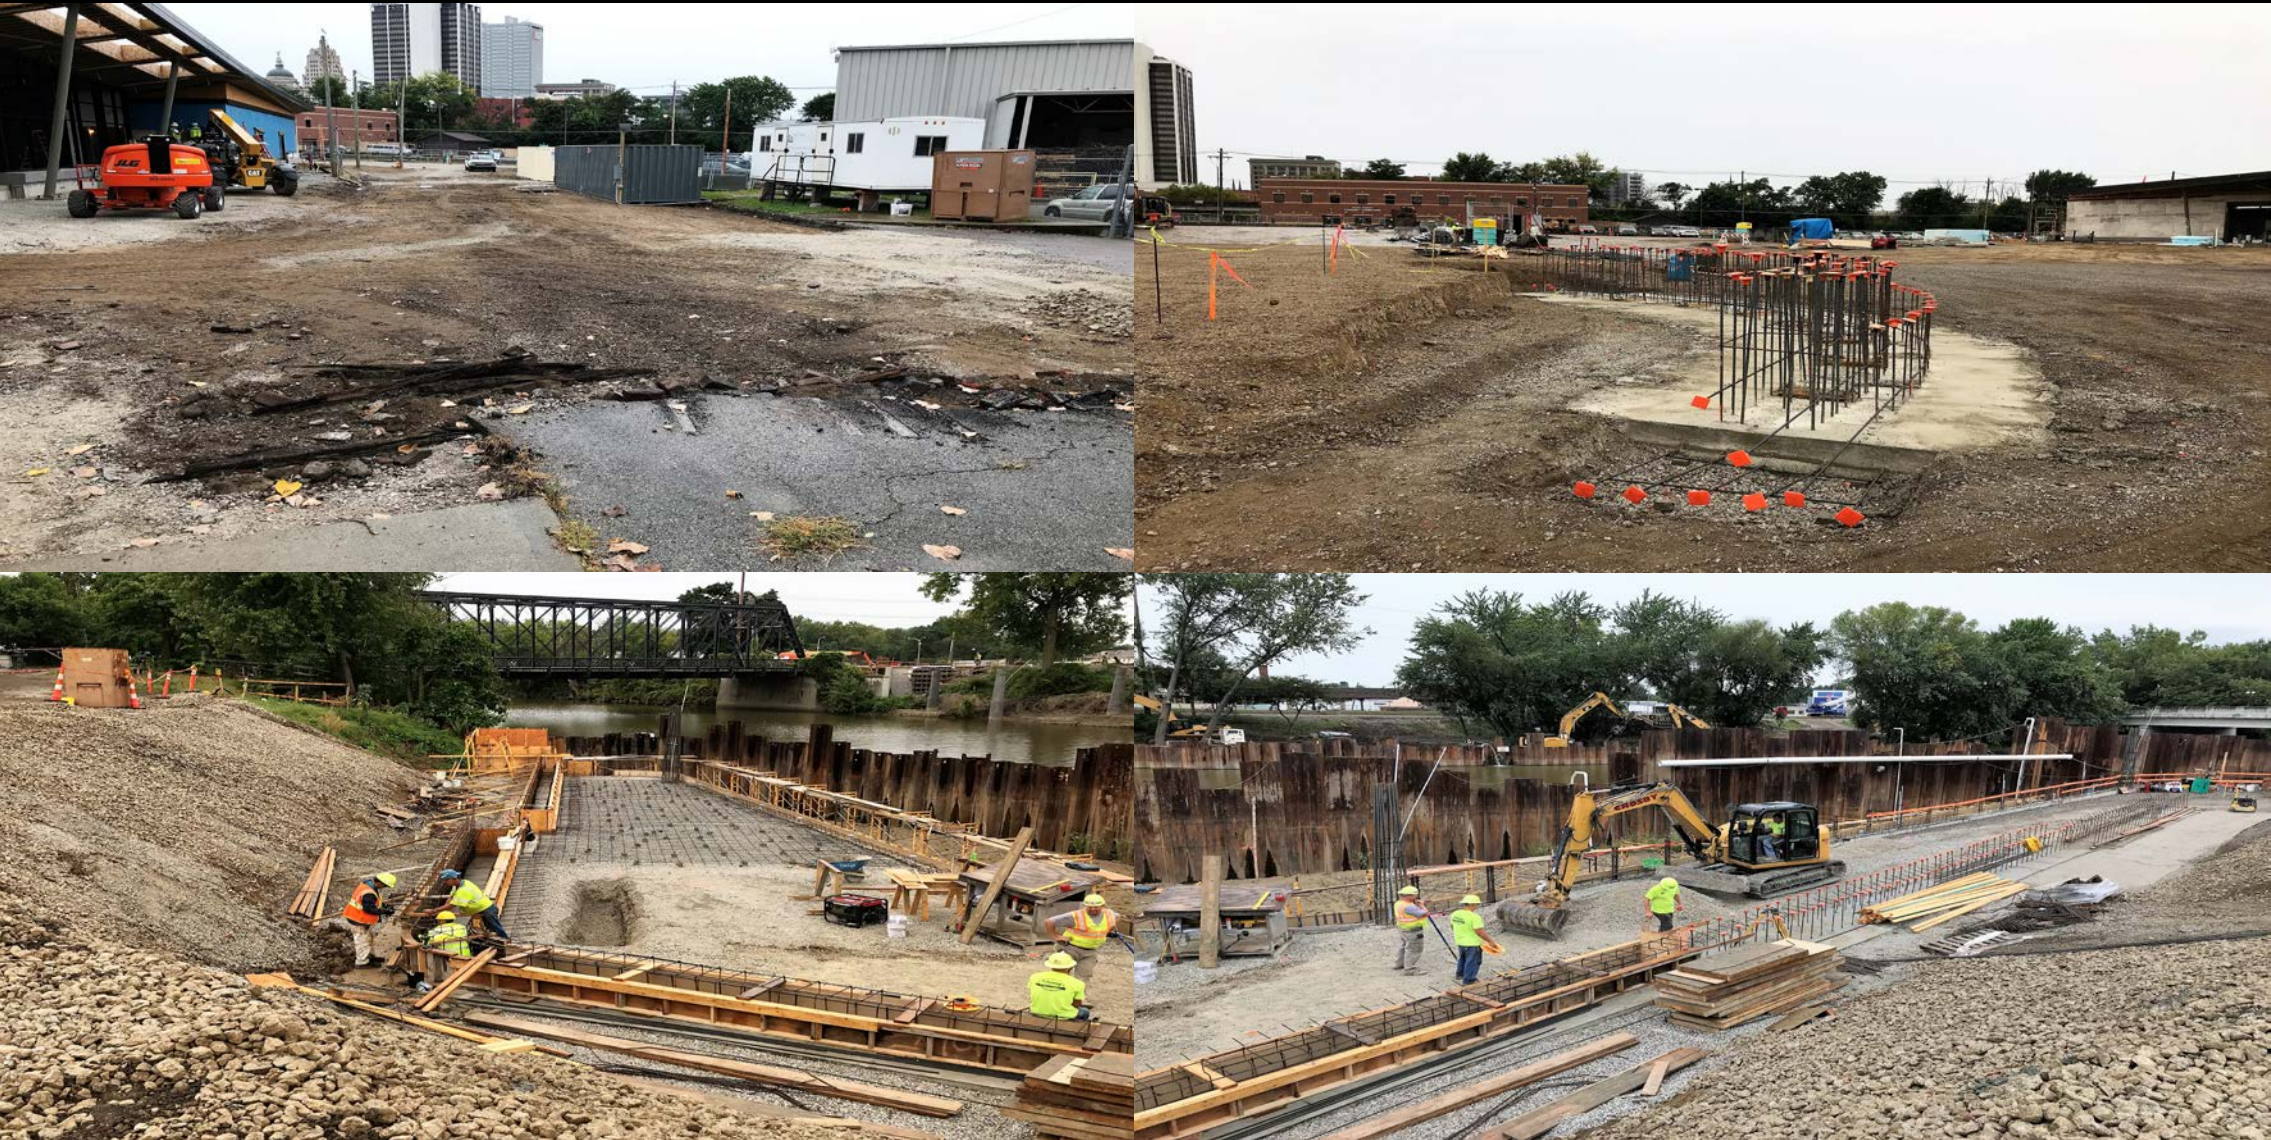

North Site Progress Photos





Fort Wayne Riverfront Phase 1

River Work North/South Shore & Misc. Site Excavation



Weekly Progress Update for Week Ending 9/9/18

North Shore Progress Photos (Continued)

